North Sea Transition Deal – Technology Mapping

Deliverables

- A structured report that addresses a comprehensive mapping of the technology gaps and innovation landscape, will be publicly available and aimed at policy makers and used to inform the NSTD Forum. The report will be developed following a review and consolidation of TLB, Accenture and other external reports, expert inputs and data. It will include industry challenges and not make policy or funding instrument recommendations.
- A cost model focused on the upstream and midstream part of the hydrogen, CCUS and offshore wind value chain.
- Presentation to NSTD Forum

Contractual Structure

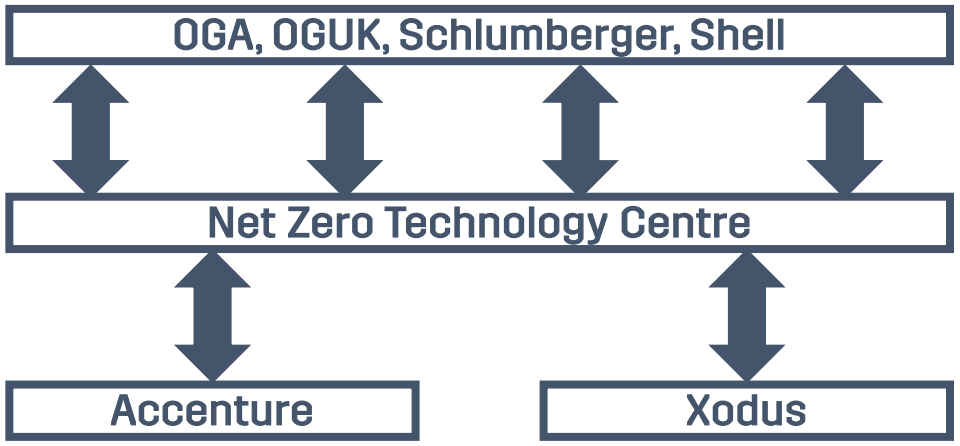

Governance

Steering Group (meet monthly)

Carlo Procaccini (OGA), Colette Cohen (NZTC), Deirdre Michie (OGUK), Kirk Miller (Shell), Mikki Corcoran (Schlumberger)

Delivery Group (meet weekly with daily input at outset)

Alana Finlayson (OGA), Chetan Laddha (Shell), Dave MacKinnon (Total), Katherine Rojas (Schlumberger), Kevin Taylor (Scottish Enterprise), Martyn Tulloch (NZTC), Stuart Broadley (EIC)

Dedicated Project Management

- NZTC PM (Jason Paterson)
- NZTC PEs (Ana Pires de Almeida, Craig Hodge)

Schedule

	Week 1	Week 2	Week 3	Week 4	Week 5	Week 6	Week 7	Week 8	Week 9	Week 10	Week 11	Week 12
	17-Jan	24-Jan	31-Jan	07-Feb	14-Feb	21-Feb	28-Feb	07-Mar	14-Mar	21-Mar	28-Mar	04-Apr
Hydrogen Workshop												
Hydrogen Workstream												
CCS Workshop												
CCS Workstream												
Offshore Wind Workshop												
Offshore Wind Workstream												
Report writing												
